App F IX 4

Previous References
ML 127-48(1,2)

1948-49
(ML)

File No 127-48
Serial Nos ~~4~~ 5

Later References
ML 143-50(3 4)

GENERAL AND REVENUE SECRETARIAT

Serial Nos Two

P. 19-L

Part B for Feb '49

SUBJECT

Construction of Sweepers' quarters at Saga

To The Prsdt, T M L Cl, Sagar

No L 9393/D 15-2-49

Conveys the approval of Govt to the work of Construction being executed through the ~~KSC~~ Municipal agency -

To The C E for R & B
" D C Shimoga &
No. L 9394-5/D 15-2-49

Construction of Sweepers Quarters at Sagar Town -

2907 ⌈2942 ⌈3256 ⌈3262

From

The President
Town Municipal Council
Sagar —

Letters No HC 117/47 48 dated 8th October 48
HC 117/47 48 dated 27th October 48

Requests sanction of the Govt to get the above work done by the Municipal agency alone —

The file relating to the GO dated 11 9 48 sanctioning an estimate for Rs 13,250/— for the construction of Sweepers' Quarters at Sagar as put up (Flag A) and the cost ordered to be met in equal proportion by the Govt and the MCC Sagar

2) The P W Dept has got to take up the above work, as the works of more than 3000/— are required to be got done But the President states that the above work may be got done thro the municipality alone by entrusting one block to each of the contractors, thereby saving much time in execution instead of entrusting at to one contractor etc

3) The president further states that the

Construction of Sweepers quarters at Sagar Town

2904 2972 3256 3262

municipality to be have to bear the usual expenditure of Rs 2000/- for supervision charges of T & D and tools and plants charges if entrusted to the above work is entrusted to the P W Dept

4) The municipal council has resolved at its meeting held on 28 9 88, to get the above work done thro the municipal agency and the president reports that steps are being taken to call for Tenders for the above work in anticipation of the Govt Sanction

5) In the above circumstances, the Dist requests sanction of Govt to entrust the the above work to the mcl agency — Sub proceedings

9/11 6) Pl obtain the estimate for Rs 13,450/- which has been furnished in this behalf Does it not include the T & D charges? Is there a municipal Engineering subordinate who can supervise this work? Otherwise how can the work be said to be done by the agency?

for 19/11/88

7) Sub to the a draft letter for appl

25/11 for 26/11/88

8) Issued as 7/12/88

3256 V3262 V4616

Construction of Sweepers quarters at Sagar

To,

The President, Town Municipal Council, Saga
No L6174 dated 7-12-48,
Calls for information

Sus A

From,

The President, Town Municipal Council, Sagar
No H C 117/47-48 dated 12th Dec 48
Forwards the estimate for Rs 13250/-
and furnishes information

9) The Pdt states that the estimate for Rs 13,250/ sanctioned in Govt order does not include the Establishment charges and plant charges

10) He says that there is no Engineering Subordinate attached for permanent in the Municipality to supervise the work of 17/1/49 Carried out through the Municipal agency, but that the work is simple and the supervision will be done by the Health Inspector and who have some experience of such work the Chief Officer, and by the President himself

B- 18-1-49

11) If the work has to be executed through the P W D, the estimate should be revised so as to include the E D P charges now that has not been done

Construction of Sweepers' quarters at Q.M.G. Estate

Taking advantage of the above
fact, the President states that the
work will be carried out thro' the
municipal agency. The works
very costly and the first have entailed
half the expenditure amounting to Rs 6,6,25/- out of
the improvement funds. Therefore during 1948-49
in order to get the money's worth,
it is necessary to get the work
executed thro' the technical agency
The request is forwarded.
If approved, the Chief Engineer for
Roads & Buildings will be consulted
on the proposal. [illegible] 18/11/49

18/1

12) It is better to get the work executed through
the P.W.D. Agency. The Chief Engineer for
Roads & Buildings may be consulted

[illegible]
TIE [illegible]
LOCAL [illegible] UNIT
3615-
20/11/49

Rs
19/11/49

[illegible] 19/11/49

13) In order to ensure the speedy progress of the work
the Mlly as a special case, may be permitted
to execute the work the estimate may be got
sanctioned.

24/11/49 [illegible] 25/11/49

4616 √5198,

Construction of Sweepers' quarters at Sagar

14) It is for orders whether the estimate may be sent unofficially to the CE for R and B for scrutiny before communicating the orders.

8/2/45 Pr 9-49 15) The estimate for Rs 13,250 for this work has been scrutinized by the C-E for R & B & returned with his memo no 33 dt 7/8/45 & (vide para 11 of the notes in Pl file 12748 - 1949)

16) Pl put up a draft letter conveying sanction to the work being executed by the Pl agency as per orders of the Minister at para 13 above

for 7/2/45

16) Submitted with a draft letter for appl thereon

10/2/45 Pr 10-49

for 11/2/45

To,

The Pdt, Town Pl of Sagar,

No L 9393/15-2-45

Conveying the approval of Govt

B

19/2/45

2907/M4

OFFICE OF THE PRESIDENT
TOWN MUNICIPAL COUNCIL 13/ca

DATED SAGAR 8th October 194 8

From

The President

Town Municipal Council

Sagar

To

The Secretary to Government

Revenue Department

Bangalore

Mr. invited for M & W

No 117
Encl 1

REVENUE SECRETARY
Vo
Date 12/10
GOVERNMENT OF MYSORE

Sir

Subject Construction of Sweepers' Quarters at Sagar

--

I have the honour to convey the greatfulness of the Municipality to the benign Government for the generous grant of s 6 625/- made for the construction of Sweepers Quarters at Sagar The Municipality has laid down a Scheme of housing all the Sweepers of this Municipality numbering 0 in all within a period of 5 years taking up 10 houses each year with the generous help of the overnment ?

As a first step towards this the Municipality is willing to bear the other half of the amount of s 6 625/- being the share of the Municipal t for the construction of 10 houes estimated o cost s 13 2 0/- As works of more than Rs 3 000/- are required to be got done through the Public orks Department as per rules laid down the unicipality feels that this work being of a ver ordinary character and as each Block of 2 houses is estimated to cost only 2 o50/- may be got done through the unicipality alone entrusting one Block to each of the contractors also saving much time in execution if it is entrusted to only one contractor The Municipality is further of opinion that if this work is entrusted to the P D the usual expenditure by way of supervision charges and tools & Plants charges, has also to be borne by the Municipality which will amount to s 2 000/- on the tender rates which will naturally be higher than the estimated rates This will be an extra expenditure which can also be saved if the same is got done by Municipal Agency as this work does not require much of technical skill

P T O

The Council has considered all the representations made on the 9-10-[illegible] to the work done by the Council generally and to obtain proper protection of Government property

As this move is calculated to benefit the Municipal finances and saves much time also an execution request will be sent as soon as a kindly accordance of Government for execution this work through the Municipal Council Investigation of kindred action I have taken as soon as all Government works will be put on hand after the Municipal Council order are received

The resolution of the Municipal Council [illegible] favour of kind perusal

Yours Faithfully

[illegible]
President

3256/ 4

3

ನಾಗರದ ಪೌರಸಭೆ

ಸಾಗರ ಪೌರಸಭೆಯ ತಾ|| ೨೬ ೧ ೧೯೬೬ ಸಾಮಾನ್ಯ/ವಿಶೇಷ ಮೀಟಿಂಗಿನಲ್ಲಿ ನಡೆಸಿದ ಕಾರ್ಯಕ್ರಮಗಳು

ಸಭೆಯ ಅಧ್ಯಕ್ಷರು — ಸರ್ವ ಶ್ರೀ H Swaminathan ಬಿ ಸಿ ಸಿ ಐ

ವಿಷಯಗಳು	ತೀರ್ಮಾನ
ಅಧ್ಯಕ್ಷರ ಆಯ್ಕೆ ಮಾಡುವ ಬಗ್ಗೆ	ಶ್ರೀ H Swaminathan ರವರನ್ನು ಅಧ್ಯಕ್ಷರನ್ನಾಗಿ ಆಯ್ಕೆ ಮಾಡಲಾಯಿತು
ಅಧ್ಯಕ್ಷರ ಆಯ್ಕೆಯ ಬಗ್ಗೆ	ಶ್ರೀ H Swaminathan ರವರನ್ನು ಅಧ್ಯಕ್ಷರನ್ನಾಗಿ ಆಯ್ಕೆ ಮಾಡಲಾಯಿತು

" ಯಜಮಾನಕೆಲ್ಲು

ಅಧ್ಯಕ್ಷರು

(ಸಹಿ) H Swaminathan
ಅಧ್ಯಕ್ಷರು
ಸಾಗರ ಪೌರಸಭೆ ಸಾಗರ

3256/M4

OFFICE OF THE PRESIDENT
TOWN MUNICIPAL COUNCIL

DATED SAGAR 27th October 194

From

The President
Town Municipal Council
Sagar

To

The Secretary to Government
Revenue Department
Bangalore

C 117/47-48

Sir

Subject

In continuation of this Office letter No. C 117/47-48 dated 9-10-1948 requesting you to kindly accord sanction of Government for getting the work of construction of Sweepers Sheds in this Town through the Municipal Agency alone in view of the circumstances mentioned therein I have the honour to further state that the limit of Rs 3 000/- upto which the Municipal Council can execute the Public works was prescribed at a time when all building materials were cheap and labour problem not as difficult as it is now The rates have gone 3 or 4 times higher than at the time when this limit was fixed by the Government If this limit is adhered to in these times of labour difficulty and abnormal rise in building materials works even of a small nature cannot be executed by the Municipalities and no progress of works can be shown and consequently improvements cannot be effected in towns expeditiously It is really high time that the Government should consider this aspect of the question which is working as a great hardship in all the Municipalities while executing improvement works in their jurisdictions and increase the limit up to which the Municipal Councils can execute works through their own agency

I therefore request you to be so good as to kindly take up this aspect of the question also while considering the question of allowing this Municipal Council to take up the constructions of the Sweepers quarters in this town

This may kindly be treated as urgent and very early orders of Government communicated

P T O

6174 3 copies 7-12-48 6 8

To

The President
Town Municipal Council
Sagar—

Subject Construction of Sweepers' Quarters in Sagar town—

Sir I am refer to your letter No IIE 117/47 48 dated 8th October 48 on the above subject, I am directed to enquire whether the Estimate for Rs 13250/— sanctioned in the G O d 11-9 48 does not include the Establishment Tools and plant charges and if so why should the Municipality not bear the Supervision charges of Rs 1000/— of the work also stated therein. There is a municipal Engineering Subordinate who can do the supervising work & if the work is entrusted to contractors by the Municipality of them instead of municipal

5

com 7

~~municipal~~ Engineering Subordinate in the Municipality ~~above~~ is requested how the work can be got done through ~~municipal~~ agency

VAP

I am to request that the estimate for Rs 13250/- may be sent along with the inspection report to above immediately.

Yours faithfully

for Secy

Ok

By

Dy

L6175- AJ 7-12-68

Copy is forwarded to the DC Shimoga, w/c to inform

By

for Revenue

By

GOVERNMENT OF HIS HIGHNESS THE MAHARAJA OF MYSORE

No L6174

General and Revenue Secretariat

Dated Bangalore 7-12-1948

FROM

The Secretary to the Governm nt of His Highness the Maharaja of Mysore
Revenue Department

To

The President,
Town Municipal Council,
Sagar

SUBJECT Construction of sweepers quarters in Sagar Town

Sir,

With reference to your letter No Hc 117/47-48 dated 8th October 1948 on the above subject, I am directed to enquire whether the estimate for Rs 13,250/- sanctioned in the Government Order dated 11th September 1948 does not include the establishment, tools and plant charges and if so why the Municipality should not bear the supervision charges of Rs 2,000/- It may also be stated whether there is a municipal engineering subordinate who can do the supervising work if the work is entrusted to contractors by the Municipality If there is no Engineering subordinate in the Municipality it may be explained how the work can be got done through the municipal agency

I am to request that the estimate for Rs 13,250/- may be sent along with the information referred to above immediately

Yours faithfully,

Sd/- Syed Abdul Aleem,

Secretary to Government,
Revenue Department

Memo No L6175 dt 7-12-48

Copy of the above is forwarded, with compliments, to the Deputy Commissioner, Shimoga District, for information

By Order,

For Secretary to Government,
Revenue Department

OFFICE OF THE PRESIDENT
TOWN MUNICIPAL COUNCIL

DATED SAGAR 14th Decemb r 1948.

From

The President

Town Municipal Council

Sagar

To

The Secretar to overnment

Revenue Dep rtment

Bangalore

Ms No 117 /4848
Encl 1

Sir

Subject

With reference to our letter No L 6174 da ed 7-12-1948 regarding the construction of Sweepers Quar ers in this Town and call ng for more in orma ion I h ve he honour to st te hat he e timate for s 13 2 0/- san tioned in the Government Or ery dated 11 h September 19-8 does not include the Establishmen tools and plant char es Und er the presen condi on build ng cons ructions are tak n up b he Contrac ors at rates varying from 25 to 40/ above the Scheduled rates even in Public Works Departm nt At that rate the actual cost of the work at 25 on an avera eover the esti-mated amount will be Rs 16 502/- Including he establishment tools and Plan charges at 12 over the Tender ra e of s 16 56 /- which will be charged by the Public Works Department if entrus ed to them the o al cos will be Rs 18 632/- out of this the Government Grant be ng onl s 6 625/- the sh re of the Municipal Expenses will be abou Rs 1 000/- If the tools nd plant charges are not incurred, the Municipality will have to bear ~~be spared~~ only Rs 10 000/- as its quo a This Municipalit having very limited finances feels hi hly burd ned wi h ano her 2 000/- towards Establishment tool nd plan charges There are no Engineering subordi-nates in this Municiaplity

As has already been reported by me the cost of each unit of 2 bu ld-ngs is only s 2 650/- The buildin is very s mple one not involving much of technical skill There is a senior Sanitar In pector in this Municipality who is trained in Engineer n works and prep ration of Estima es There is a 1s Grade Chief Officer or ing in this Municipality re has

P T O

has also been train d in he En neerin Dep rtmen The es mates and plans enclos d herew h h ve all been p ep re n h s office by the senior S nit ry Inspector The ha e a so been ful ~~Supervised~~ Scrutinized d b the En ineer - in Dep rtmen Supervision of orks are not onl done b these Officers but freq ~~uen~~ supervision is also done o he undersi ned a ever step before pass n an bill

Further the l nicipality feels that much me can b saved apart from saving money if the works are t done throu h the l nicipal enc ov effective supervi ion ov r he work as there are not man works apart from th s The s eeper will also be accomod ed ver e rl if these quarters are ot co pleted l ~~ V~~ n e he Co ncil is r keen b ut providin amenities eep rs ver earl it hopes o achieve this aim if he works are ot done through the l nicipal ency

Therefore I reque t ou to be so ood as o kindly accord very early s nction of Gov rnment to the proposals of this l nicipal Co ncil

The e~ mate or s 1 0/- prep red n this office with the necessary plan are here ith enclosed for favour of k nd perusal

Yours F ithfull

H Swalingaloba

Presid n

VIF

[M A M 69]
L B 11

Sagar Town MUNICIPALITY [Rule 245

PUBLIC WORKS DEPARTMENT

Detailed Estimate

Work Construction of Twin houses for labourer class.

Detail of work	Numbe	Measurement: Len th	Breadth or thick ness	Height or depth	Contents	Total quantity of each description of work	Rate Rs	a	p	Cost Rs	a	p	Rema ks
Excavation in hard gravelly soil													
for the foundation													
walls all round	1	79½	2½	1½	300	cft							
cross wall	1	15'	1¾	1½'	40	"							
Verandah wall	1	35¾	2½'	1½'	135	"							
Bathroom all round	1	23½'	1¼	1'	30	"							
" — cross wall	1	5½	1¼	1'	7	"							
Walls of W closet all round	1	16½'	1¼'	1'	20	"							
					532 cft or	20 cyd		8		10			
1:4:8 Cement Concrete													
for foundation walls all round	1	79½	2½'	½'	100	cft							
cross wall	1	15'	1¾'	½'	13	cft							
Verandah walls	1	35¾'	2½'	½'	45	cft							
					158	cft	1			158			
Filling in foundation and Basement with Kutcha clay - Walls all round	1	79½'	2	2'	318	cft							
	1	15½'	1¼'	2'	39	"							
	1	35¾	2'	2'	143	"							
	1	23½'	1¼'	2'	59	"							
	1	5½'	1¼	2'	14	"							
	1	16½'	1¼'	2'	41	"							
	1	2'	1¼	1'	3	"							
Earthon wall in the Kitchen	2	7½'	1¼'	1'	19	"							
Superstructure													
Walls all round	1	79½'	1½'	9'	1080	"							
Cross Walls	1	16	¾'	9'	108	"							
Gables	1	16/2	¾'	5'	30	"							
"	2	16/2	1½'	5'	120	"							
					1111		C	0		168			

2919 /

Detail of work	Number	Measurement: Length	Breadth or thickness	Height or depth	Contents	Total quantity of each description of work	Rate Rs	a	p	Cost Rs	a	p	Remarks
partition Wall in the kitchen	2	7½'	3/4'	6'	67½ Cft		15	F	-	168			
walls around Bath	1	23½	3/4'	7½'	135 Cft								
" " " W C	1	17'	3/4'	6'	77 "								
partition Wall in W C	1	2½'	3/4'	6	12 "								
" " Bath	1	6'	3/4'	7½'	34 "								
Gables in Bath	3/2	6'	3/4	1½'	10 "								
				Total		2309 Cft							
Deductions for doors	2×2	2½'		6'	60 "								
" windows	2×2	2'		4'	32 "								
Ventilators	2×3	2½	-	1½'	23 "								
Door Opening in bath	2	2		6	24 "								
					139								
Balance	2309 − 139			=	2170 Cft		-	8	-	1085	-	-	
4) providing Jungle wood doors with 3'×4' frame battan Shutters, providing & fixing complete	2×2	2½'	-	6'	60 Sft		2	8		150			
5) providing F W windows with 3'×4' frame ½ M S bars battan Shutters painting complete	2×2	2'	-	4'	32 Sft		3			96	-	-	
6) providing R C C Ventilators fixing in position	2×3	2½'	-	1½'	22½ Sft		1	8	-	34			
7) providing B S Slab Lintels 6" including dressing and fixing complete													
over doors	4	4	1½'		24 Sft								
over windows	4	3½'	1½'		21 "		-						
over Ventilators	6	4'	1½'		36 "								
over bath Room opening	2	3½'	3/4'		6 "								
					87 Sft		1	8		131			
8) Mud plastering with 2 coats of painting complete													
walls around	1	73½'	-	9'	671 Sft								
Cross Wall	1	16	-	9	144 "		C			1664			

Detail of work	Number	Measurement: Length	Breadth or thickness	Height or depth	Contents	Total quantity of each description of work	Rate Rs	a	p	Cost Rs	a	p	Remarks
Gables	4×½	16'	—	5'	160	15	1	—	—	1664	—	—	
Dashhon Wall	2×2	8'	—	6'	192								
Bathroom alrcund	2	22	—	7½	330								
					1497 Sft								
Deductions for doors	2×½	2½'	—	6'	15								
windows	4×½	2	—	4'	16								
Vent Cabins	6×½	2½'	—	1½'	11								
Bathroom Openings	2×½	2'	—	6	12								
					54								
Balance for plastering		1497 - 54	=		1443	sft							
					14 43 Sqrs		3			43			
1) plastering with cement mortar outside	1	85'	—	9'	765	Sft							
	2	15'	—	6'	180								
					945								
deduct as per above	9 4 5 - 5 4				891	sft							
					8 91	Sqrs	7			63			
2) Fungle wood workgal and fixings with 2 coats of wood oiling													
Bressmer	1	24'	1/3"	½'	4	cft							
Ridge piece	1	24'	1/3'	5/12	3 33	cft							
wall plates	2	24'	1/4'	⅓'	4	cft							
Common Rafters	11×2	16'	5/24	⅓'	24 34								
— " — verandah	7	6	5/24	⅓'	3								
					3867	cft							
add extra required					1 33								
					40	cft	7			280			
11) Roofing with first class mangalore tile and teak wood rafters	2	24'	16'		768	sft							
over bath	1	6	15'		90								
					858	sqrs	50			430			
2) providing ridge tile set in cement	1	24'			24	rft	1			24			
Inserts										2504			

ABSTRACT OF THE FOREGOING ESTIMATE

Quantity	Description of work	Rate Rs	a	p	Per	Amount Rs	a	p	Remarks
	Total Rs								

I hereby certify that I have carefully measured the work required to be done and that at present so far as can be foreseen, everything required for the work is included in the estimate

Date Sub Overseer Overseer

I have carefully examined this estimate at the site of work and it appears to include everything which I consider necessary for completing the work

Rates and calculation checked by Date *Municipal Engineer*

Date

Vice President

WD 06736—GPB—7 000—19 7 44

Detail of work	Number	Measurement: Length	Breadth or thick ness	Height or depth	Contents	Total quantity of each description of work	Rate Rs a p	Cost Rs a p	Remarks
3) Flooring with							B F	2304	
good gravel 6" thick									
2 Coats covering with									
Hall	2	10'	10'		200	Sft			
Kitchen	2	10'	6'		120	"			
Verandah	1	21'	6'		126	"			
					546	"			
					5 sq	Sqr	2 8	14	
4) Flooring with									
1 4 8 Cement Concrete									
2½" thick and hp									
plastered with									
Cement mortar	2	7½'	6'		90	Sft			
for bath and W C					1	Sqr	3s	3s	
5) Cut latrine in									
Cement mortar 1 3	3	1½'	1½'	7'	48	Cft	= 10	30	
1 6 for front pillars									
6) pointing with									
Cement mortar 1 to 1	1	85	1'	-	85	Sft			
basement					1	Sqr	6	6	
7) Miscellaneous & unforeseen charges								2589	
								61	
Thirteen hundred and fifty rupees only					Cost of one Block		Total	2650 - 5 Blocks 13250 : 0	

Received Rupees Thirteen thousand two hundred fifty only

Sd/- 1-5

CHIEF OFFICER
TOWN MUNICIPAL COUNCIL SAGAR

24/4/18

chd for 13250/=

Rs Sixty 5 p IW

President
TOWN MUNICIPAL COUNCIL
SAGAR

Sd/- K Vasanta Madhava Rao
23/4/18

ABSTRACT OF THE FOREGOING ESTIMATE

Quantity	Description of work	Rate Rs	a	p	Per	Amount Rs	a	p	Remarks
	Total Rs								

I hereby certify that I have carefully measured the work required to be done and that at present so far as can be foreseen everything required for the work is included in the estimate

Date Sub Overseer Overseer

I have carefully examined this estimate at the site of work and it appears to include everything which I consider necessary for completing the work

Rates and calculation checked by
Date

Date *Municipal Engineer*

Vice President

WD 06736—GPB—7 000—19 7 44

15

CHEAP TWIN QUARTERS FOR LABOUR CLASS PEOPLE

Scale 8'=1'

V VENTILATORS
W - WINDOWS
D - DOORS

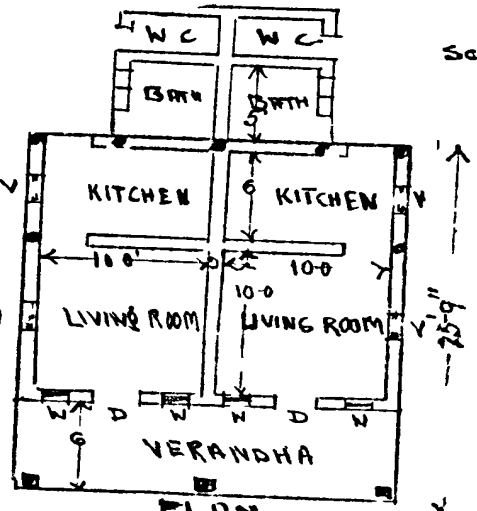

PLAN

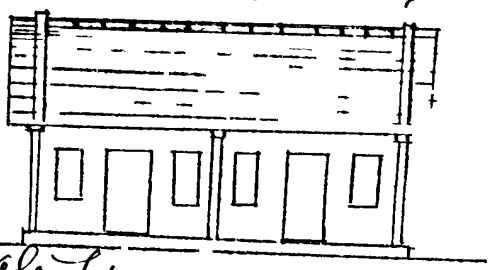

FRONT ELEVATION

By

K Vasanta Madhavarao
Sanitary Inspector
Sagar Town
23-4-48

President
CHIEF OFFICER,
MUNICIPAL COUNCIL, SAGAR

5198/ml 16

OFFICE OF THE PRESIDENT
TOWN MUNICIPAL COUNCIL 17/1
DATED SAGAR 194

From

The President

Town Municipal Council

Sagar

To

The Secretary to Government

Revenue Department,

Bangalore

No H C 117
Encl 47-48

Sir

Subject

In continuation of this office correspondence ending with letter No H C 117/47-48 dated 14-12-1948 on the matter of permitting this Municipality to execute the work of the construction of Sweepers Shed for which a generous grant has also been sanctioned by Government etc I have the honour to state that if the work is not entrusted to the contractors very early there is no possibility of its completion by the end of the Official year in which case providing of facilities to the sweepers will be postponed The entire Scheme of providing 50 house within a period of 5 years cannot also be carried out as per Programme if the present blocks are not completed within the close of the official year

I therefore request you to be so good as to kindly accord final orders of the Government very early taking the circumstances explained in my previous report into consideration and also viewing it from the point of financial condition of the Municipality

This may kindly be treated as urgent

Yours Faithfully
H Swamigappa
President

OFFICE OF THE MINISTER FOR LOCAL SELF-GOVERNMENT
D 29/1/49

VAK The main file has been subd to the Minister for L S G on 20-1-48 with D No 4616 The return of the file will be awaited. 25/1/49 Pr recvd

enc: with two kind orders of the Minister for L Sg

P. A to the Minister for L Sg 29/1/49

PTO

17

The relevant file has been sent
with orders of the Monetary Unit which was
(35 9/4/49 office note Docket No 3645 Dated 1 2 49

Mr Malleffa

7/IX/49

Dupl

To, Dtd 127-48-S L9393 15-2-49 18

The Pdt, Town Municipal Sagar

Subject - Construction of Sweepers' quarters at Sagar

Sir, With reference to the correspondence ended with your letter No H e 117/47-48 dated nil (received on the 12th January 1948) on the above subject, I am directed to convey the approval of Govt to the work being executed speedily through the Municipal agency as suggested necessary further action being taken to expedite the work by you.

Yours faithfully,

If Constn of Sweepers' quarters at Sagar sanctd in Fo no 1 2841 4/1 127 48 - dated 11 9 48

L9396-5 15-2-49

Copy forwarded w/c to

1) The C2 for N/B
2) The DC, Sagar for Secy to Govt

Pr 11-2-49

for General Secy

Pr 11-2-49

GOVERNMENT OF HIS HIGHNESS THE MAHARAJA OF MYSORE

General and Revenue Secretariat

No L9393 *Dated Bangalore* 15 2 - 1949

FROM

The *Secretary to the Government of*
His Highness the Maharaja of Mysore
General Department

The President,
Town Municipal Council,
Sagar.

SUBJECT Construction of sweepers' quarters at Sagar

Sir,

With reference to the correspondence ending with your letter No Mc.117/47-48 dated nil (received from here on the 12th January 1949) on the above subject, I am directed to convey the approval of Government to the work of construction of sweepers quarters at Sagar sanctioned in Government Order No I.2641-4/M1 127-48-2 dated 11th September 1948 being executed through the Municipal agency as requested Necessary further action maybe taken to expedite the work in question

Yours faithfully,

Sd/- Mir Safdar Hussain,
Secretary to Government,
General Department.

p t o

20

Memo No 19394-5 dated, the 15-2-29

Copy of the foregoing is forwarded, with compliments,
to the (1) Chief Engineer for Roads and Buildings and
(2) The Deputy Commissioner, Shimoga District

By Order,

For Secretary to Govern
Gereral Department

DFT.

Notes ——————— 5 Pages

Correspondence —— 20 Pages
